

**Date:** 3/21/2022 **Author:** RAY MIRELEZ **Project:** N FIRST ST SELAH JOHN CAMPBELL CHERVENELL CONSTRUCTION TCP#1

**Comments:**



THIS TRAFFIC CONTROL PLAN IS TO PROVIDE A DOUBLE RIGHT LANE CLOSURE FOR CREW TO COMPLETE SCOPE OF WORK ALL SIGNS AND DEVICES WILL BE ACCORDANCE WITH MUTCD

**SIGN SPACING**

ARTERIALS AND COLLECTORS	45 / 55 MPH	500'
ARTERIALS AND COLLECTORS	35 / 40 MPH	350'
ARTERIALS AND COLLECTORS	25 / 30 MPH	200'
RESIDENTIAL STREETS	25 MPH OR LESS	100'

ALL SIGNS ARE 48" X 48" BLACK ON ORANGE UNLESS OTHERWISE DESIGNATED



**Manifest**

- 29 x Cone
- 4 x W20-1 road work ahead
- 4 x W20-3 road closed ahead
- 2 x M4-10 Detour M4-10L
- 2 x M4-10 M4-10
- 2 x R11-2 road closed R11-2
- 2 x W20-2 detour ahead
- 2 x W4-2 road narrows
- 1 x Arrowboard (Chevron)
- 1 x Barrier
- 1 x R11-4 road closed to thru traffic
- 1 x W20-5 left lane closed ahead
- 1 x W20-5 right lane closed ahead

1985

46°39'25.92" N 120°31'41.74" W



Date: 3/21/2022 Author: RAY MIRELEZ Project: N FIRST ST SELAH JOHN CAMPBELL CHERVENELL CONSTRUCTION TCP#2

www.invarion.com

**Comments:**

THIS TRAFFIC CONTROL PLAN IS TO PROVIDE A DOUBLE RIGHT LANE CLOSURE FOR CREW TO COMPLETE SCOPE OF WORK ALL SOGNS AND DEVICES WILL BE ACCORDANCE WITH MUTCD




SIGN SPACING		
ARTERIALS AND COLLECTORS	45 / 55 MPH	500'
ARTERIALS AND COLLECTORS	35 / 40 MPH	350'
ARTERIALS AND COLLECTORS	25 / 30 MPH	200'
RESIDENTIAL STREETS	25 MPH OR LESS	100'
ALL SIGNS ARE 48" X 48" BLACK ON ORANGE UNLESS OTHERWISE DESIGNATED		

Manifest
51 x Cone
5 x W20-1 road work ahead
2 x R3-2 No Left Turn
2 x W20-5 left lane closed ahead
2 x W4-2 road narrows
1 x Arrowboard (Chevron)
1 x W20-5 right lane closed ahead

ATTENTION PROJECT TEAM: We will continue to look for opportunities to improve on the dates and sequences shown herer. All dates are subject to change and need to be confirmed with Lucas Schmidt 509-727-1806

ID	Task Mode	Task Name	Duration	Start	Finish	January							February				March				April				May				June				July			
						12/26	1/2	1/9	1/16	1/23	1/30	2/6	2/13	2/20	2/27	3/6	3/13	3/20	3/27	4/3	4/10	4/17	4/24	5/1	5/8	5/15	5/22	5/29	6/5	6/12	6/19	6/26	7/3	7/10		
1		<b>John Campbell Primary</b>	<b>161 days</b>	<b>Fri 11/19/21</b>	<b>Wed 7/6/22</b>																															
62		Phase 1 Asphalt Painting (Spring Break)	2 days	Mon 4/4/22	Tue 4/5/22																															
76		<b>Home Ave (East)</b>	<b>12 days</b>	<b>Wed 3/23/22</b>	<b>Thu 4/7/22</b>																															
77		Traffic Control	1 day	Wed 3/23/22	Wed 3/23/22																															
78		Excavation	2 days	Thu 3/24/22	Fri 3/25/22																															
79		Bases	2 days	Thu 3/24/22	Fri 3/25/22																															
86		Sawcut	1 day	Mon 3/28/22	Mon 3/28/22																															
81		Curb & Sidewalk Prep	1 day	Tue 3/29/22	Tue 3/29/22																															
80		Demo & UG Utilities	2 days	Tue 3/29/22	Wed 3/30/22																															
82		Curb	1 day	Wed 3/30/22	Wed 3/30/22																															
83		Sidewalk Pour	1 day	Thu 3/31/22	Thu 3/31/22																															
84		Pave (plant dependent)	3 days	Mon 4/4/22	Wed 4/6/22																															
85		Set Traffic Poles	1 day	Thu 4/7/22	Thu 4/7/22																															
61		<b>Install Pour in Place (Spring Break)</b>	<b>5 days</b>	<b>Mon 4/4/22</b>	<b>Fri 4/8/22</b>																															
25		<b>Sunset School</b>	<b>38 days</b>	<b>Mon 2/28/22</b>	<b>Wed 4/20/22</b>																															
29		Leslie & Campbell Roof Abatement	10 days	Mon 2/28/22	Fri 3/11/22																															
30		Abate East Half	10 days	Thu 3/10/22	Wed 3/23/22																															
26		Demo East Half	10 days	Thu 3/24/22	Wed 4/6/22																															
27		Abate West Half	10 days	Thu 3/24/22	Wed 4/6/22																															
28		Demo West Half	10 days	Thu 4/7/22	Wed 4/20/22																															
33		<b>Bus Loop Completion</b>	<b>19 days</b>	<b>Fri 3/25/22</b>	<b>Wed 4/20/22</b>																															
34		Survey	1 day	Fri 3/25/22	Fri 3/25/22																															
36		Prep for Curb	1 day	Mon 3/28/22	Mon 3/28/22																															
35		Curbing	1 day	Tue 3/29/22	Tue 3/29/22																															
39		Excavate Benches & Prep Sidewalk	2 days	Mon 4/4/22	Tue 4/5/22																															
40		Rebar Sidewalks	1 day	Wed 4/6/22	Wed 4/6/22																															
42		Set Bollards	2 days	Thu 4/7/22	Fri 4/8/22																															
43		Form & Pour Benches	3 days	Wed 4/6/22	Fri 4/8/22																															
37		Demo Aphalt & Gravel Prep	1 day	Fri 4/8/22	Mon 4/11/22																															
38		Pave Bus Loop (Plant Opening Dependent)	1 day	Mon 4/11/22	Mon 4/11/22																															
44		Pour Sidewalk	1 day	Mon 4/11/22	Mon 4/11/22																															
41		Sandblast & Seal	2 days	Tue 4/19/22	Wed 4/20/22																															
87		<b>Home Ave (West) / First Street</b>	<b>14 days</b>	<b>Thu 4/7/22</b>	<b>Tue 4/26/22</b>																															
89		Move Traffic Control	1 day	Thu 4/7/22	Thu 4/7/22																															
90		Excavation	2 days	Thu 4/7/22	Fri 4/8/22																															
92		Bases	2 days	Thu 4/7/22	Fri 4/8/22																															
88		Saw cut (First Street)	1 day	Mon 4/11/22	Mon 4/11/22																															
93		Survey	1 day	Tue 4/12/22	Tue 4/12/22																															
91		Demo Curb, sidewalk & Pavement	4 days	Tue 4/12/22	Fri 4/15/22																															
94		Curb Prep	3 days	Thu 4/14/22	Mon 4/18/22																															
97		Curbing	2 days	Tue 4/19/22	Wed 4/20/22																															
95		Pave Prep	3 days	Thu 4/21/22	Mon 4/25/22																															
96		Pave	1 day	Tue 4/26/22	Tue 4/26/22																															
107		<b>Bartlett</b>	<b>7 days</b>	<b>Mon 4/18/22</b>	<b>Tue 4/26/22</b>																															
108		Sawcut Inc. Play Ground	1 day	Mon 4/18/22	Mon 4/18/22																															
112		Traffic Control	1 day	Mon 4/18/22	Mon 4/18/22																															
109		Water Tie Ins	2 days	Tue 4/19/22	Wed 4/20/22																															
110		Gas Removal	1 day	Thu 4/21/22	Thu 4/21/22																															

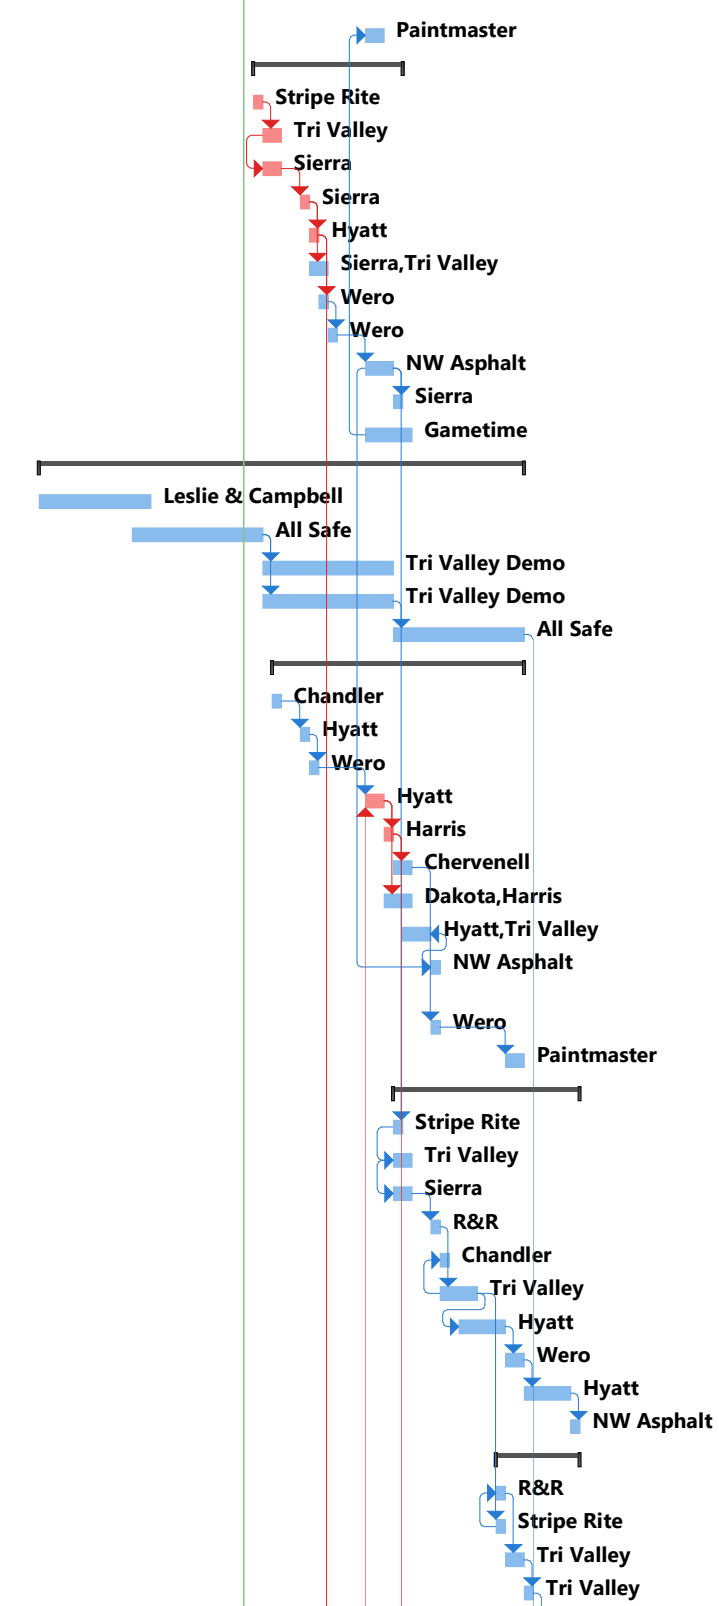

Project: John Campbell Schedu  
Date: Tue 3/22/22

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	

