ID	Task Name	Duration	Start	Finish
1	Pre Con	1 day	Mon 3/7/16	Tue 3/8/16
2	Mob in	4 days	Mon 3/14/16	Mon 3/21/16
3	Start Date	1 day	Mon 3/21/16	Tue 3/22/16
4	Grind trench from Southern to Riverview	1 day	Mon 3/21/16	Tue 3/22/16
5	Pothole crossing from Southern to Riverview	2 days	Tue 3/22/16	Thu 3/24/16
6	Install main line from southern to riverview	3 days	Thu 3/24/16	Wed 3/30/16
7	Install services from southern to riverview	3 days	Wed 3/30/16	Tue 4/5/16
8	Test pipe from southern to riverview	3 days	Tue 4/5/16	Mon 4/11/16
9	Grind trench from Riverview to Valleyview	1 day	Tue 4/5/16	Wed 4/6/16
10	Pothole crossings from Riverview to Valleyview	1 day	Wed 4/6/16	Thu 4/7/16
11	Make main line connection at Southern	1 day	Mon 4/11/16	Tue 4/12/16
12	Make service connections from southern to Pleasant	1 day	Tue 4/12/16	Wed 4/13/16
13	Make main line connection at Pleasant	1 day	Wed 4/13/16	Thu 4/14/16
14	Make service connections from Pleasant to Riverview	1 day	Thu 4/14/16	Mon 4/18/16
15	Install main line from Riverview to Valleyview	2 days	Mon 4/18/16	Wed 4/20/16
16	Install services from Riverview to Valleyview	2 days	Wed 4/20/16	Mon 4/25/16
17	Test Pipe from Riverview to Valleyview	3 days	Mon 4/25/16	Thu 4/28/16
18	Make main line conncection at Riverview	1 day	Thu 4/28/16	Mon 5/2/16
19	Make service connections from Riverview to Valleyview	1 day	Mon 5/2/16	Tue 5/3/16
20	Make mainline connection at Valleyview	1 day	Tue 5/3/16	Wed 5/4/16
21	Cut trench, clean up edges, prep for grinding	3 days	Wed 5/4/16	Tue 5/10/16
22	Grind 3rd street	1 day	Tue 5/10/16	Wed 5/11/16
23	Overlay 3rd street and patch trenches	1 day	Wed 5/11/16	Thu 5/12/16
24	Substainal Completion	1 day	Fri 5/13/16	Mon 5/16/16
25	Fog seal	3 days	Thu 5/12/16	Tue 5/17/16
26	De mob and Paint road	4 days	Tue 5/17/16	Tue 5/24/16

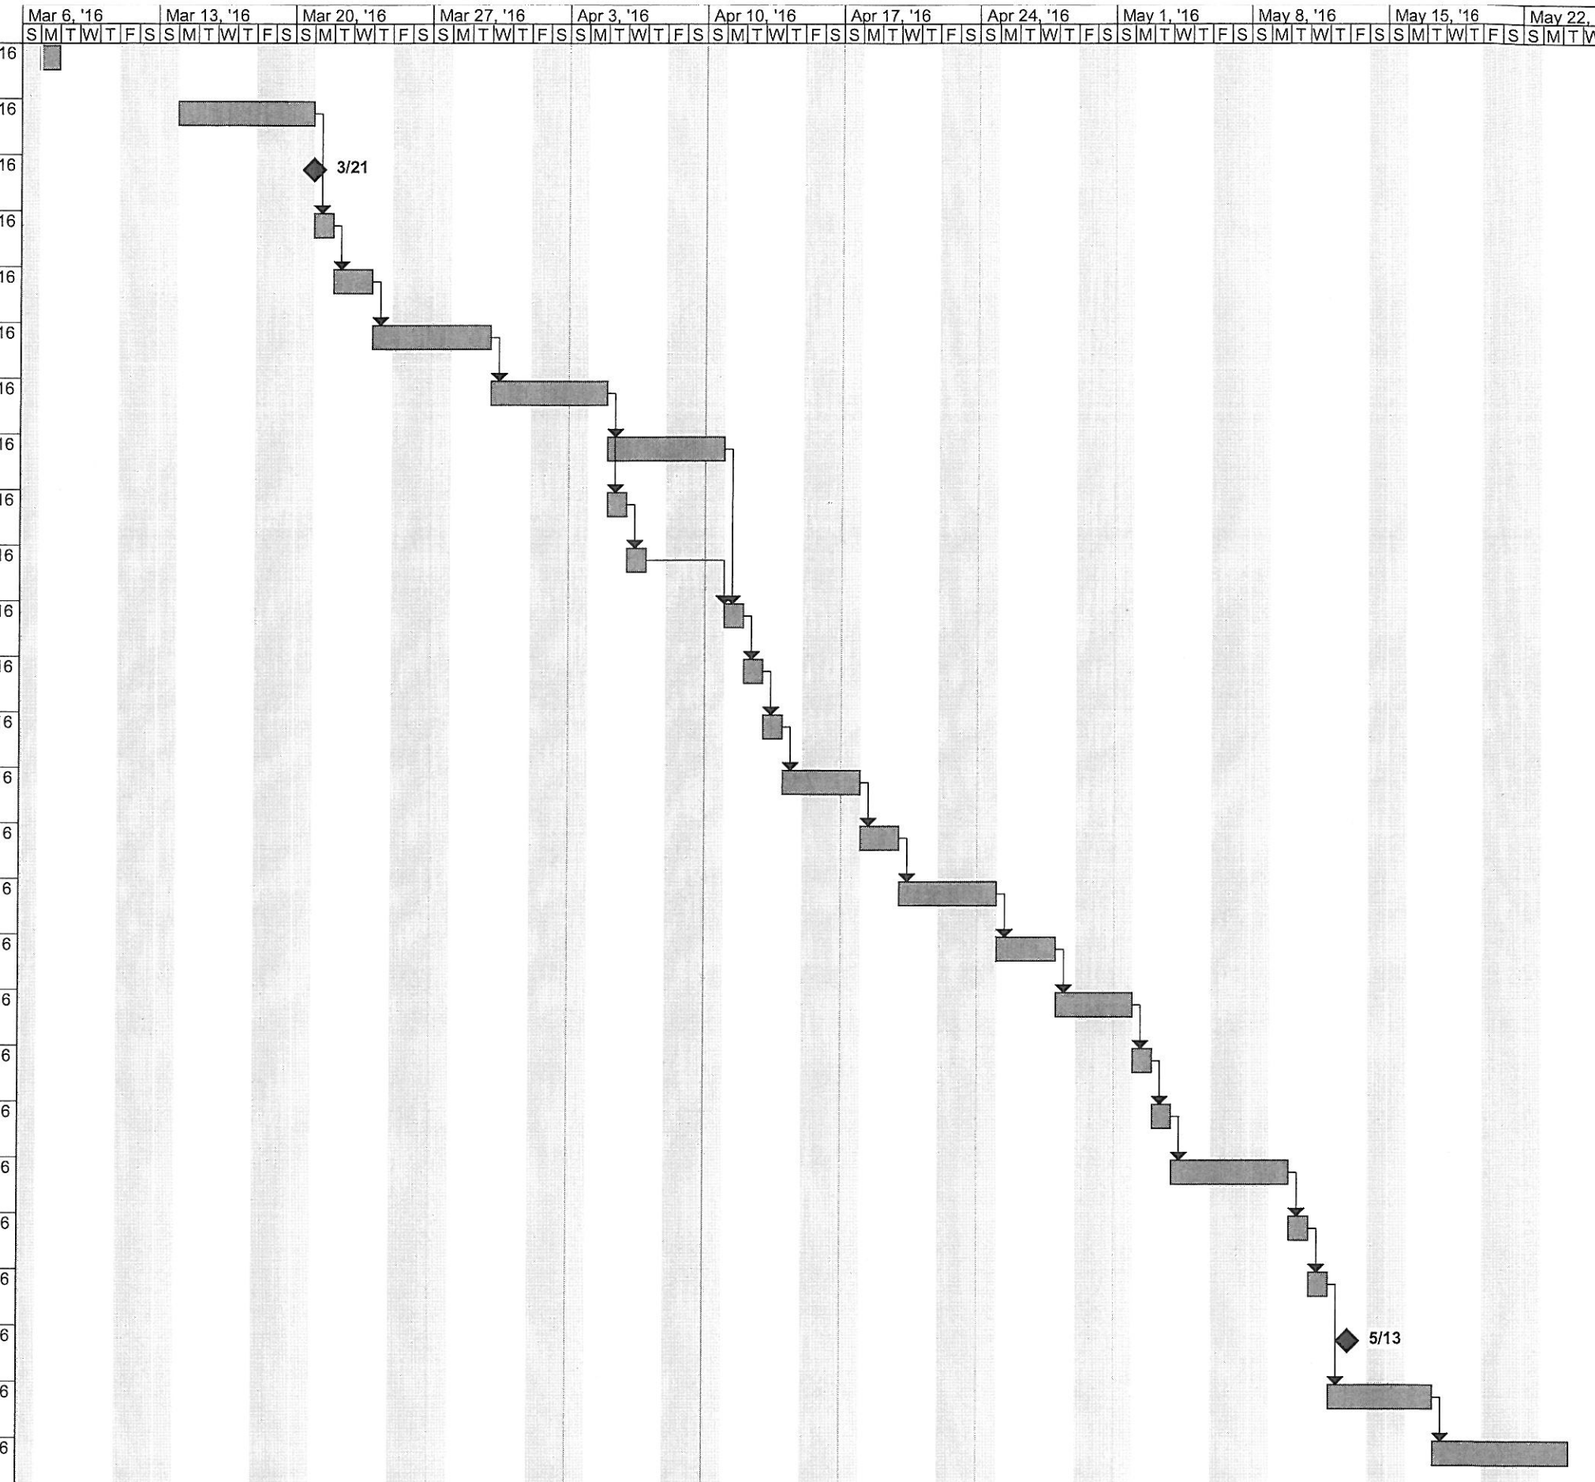

Project: Original Plan
Date: Mon 3/7/16

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
